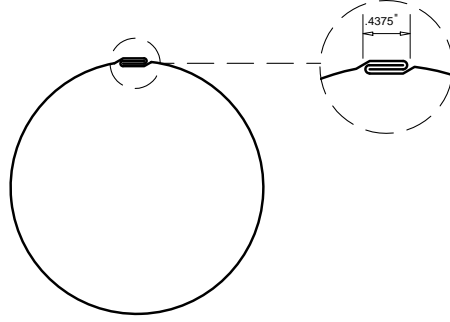# ROUND DOWNSPOUT
+ ACCESSORIES

ELBOWS ③

75 Deg. Std or

.4375"

ROUND DOWNSPOUT
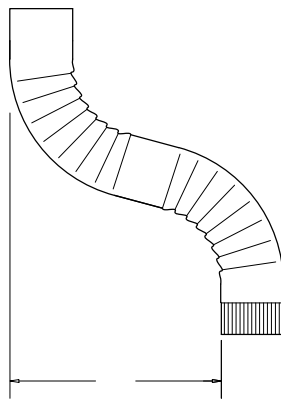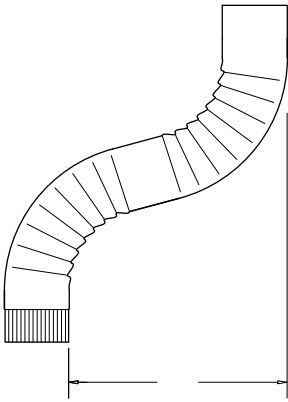
10'
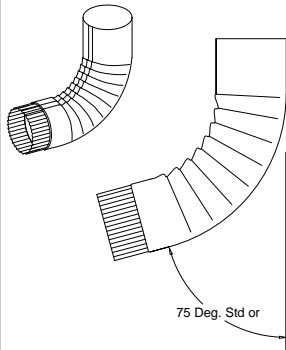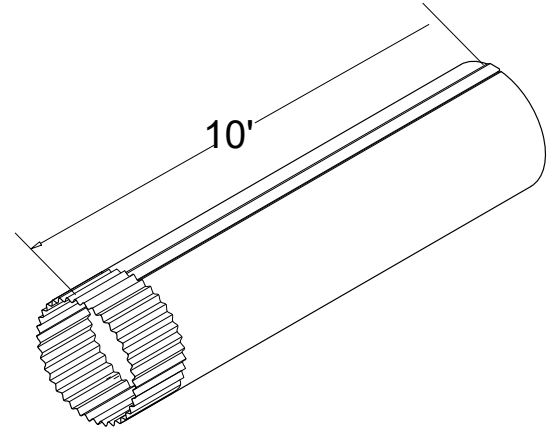
ONE-PIECE OFFSETS ③

"UP" STYLE (EAVE)

**"DOWN" STYLE (LEDGE)**

OUTLET TUBES

TYPE A-FLAT TOP

TYPE B -HALF-ROUND TOP

STRAPS

1.625" WIDE WITH .25" HEM

🧵 SIZE:

- ☐ 3" ROUND DOWNSPOUT ①
- ☐ 4" ROUND DOWNSPOUT
- ☐ 5" ROUND DOWNSPOUT
- ☐ 6" ROUND DOWNSPOUT
- ☐ 7" ROUND DOWNSPOUT ③
- ☐ 8" ROUND DOWNSPOUT ③
- ☐ 9" ROUND DOWNSPOUT ③
- ☐ 10" ROUND DOWNSPOUT ③

📋 NOTES:

① Not U[U]U Y]o &&[U ghYY cf "5 Ui a]oi a "

② For products/material not listed, please inquire.

③ Elbows and offsets that are 7" and larger will be mitered and caulked.

🎴 MATERIAL②

22GA STEEL
24GA STEEL
26GA STEEL (limited color availability)

22GA STAINLESS STEEL
24GA STAINLESS STEEL
26GA STAINLESS STEEL

.032 ALUMINUM
.040 ALUMINUM
.050 ALUMINUM

16OZ COPPER
20OZ COPPER

🎨 COLOR:_____

✂ QUANTITIES:

_____ LINEAL FEET@ 10 '-0" LENGTHS

_____OUTLETS STYLE A _____STYLE B_____

_____ELBOWS (STD. 75°)③

_____ELBOWS (CUSTOM DEGREE) ____°

_____ONE-PIECE OFFSETS   " OFFSET AMOUNT ③

_____STRAPS (STANDARD =2 PER 10' DOWNSPOUT)

📋 PRINT APPROVED BY:

_____   _____
(SIGNATURE)   (DATE)

A SIGNED PRINT APPROVAL SIGNIFIES A CUSTOMER HAS
VERIFIED ALL DIMENSIONS, SIZES, QUANTITIES, AND
MATERIAL TYPES.
FABRICATION WILL PROCEED ONLY AFTER RECEIPT OF
SIGNED PRINT APPROVAL

ℹ PROJECT INFORMATION

_____
(PROJECT NAME)

_____
(ARCHITECT)

_____
(CUSTOMER)

_____
(REPRESENTATIVE/ DISTRIBUTOR)

Roof Drainage Components & Accessories, Inc

📍60 Don Wesbrook Ave North
   Jasper, GA 30143

📞706-692-7333

✉ sales@rdcaa.com

🌐 www.rdcaa.com
